

Project description

hybrid




SimulTrain

Project description

Project name	Online Service Deployment
Estimated duration	11 weeks
Milestone	<ol style="list-style-type: none">1. Data Base & Marketing Sprint2. eShop Design & Development Sprint3. Release Sprint (end of project)
Team	<ul style="list-style-type: none">– Sue, Fred and Tim– Other people as necessary
Description	In accordance with the new marketing strategy, management wishes to provide our customers with an online interactive service. This will allow customers to follow-up and control orders without the intervention of either the customer service or the accounting departments. The customer representative is the Product owner. The list of product backlog items and a budget for the first stage have been defined. The core team has been established.

Organization Chart

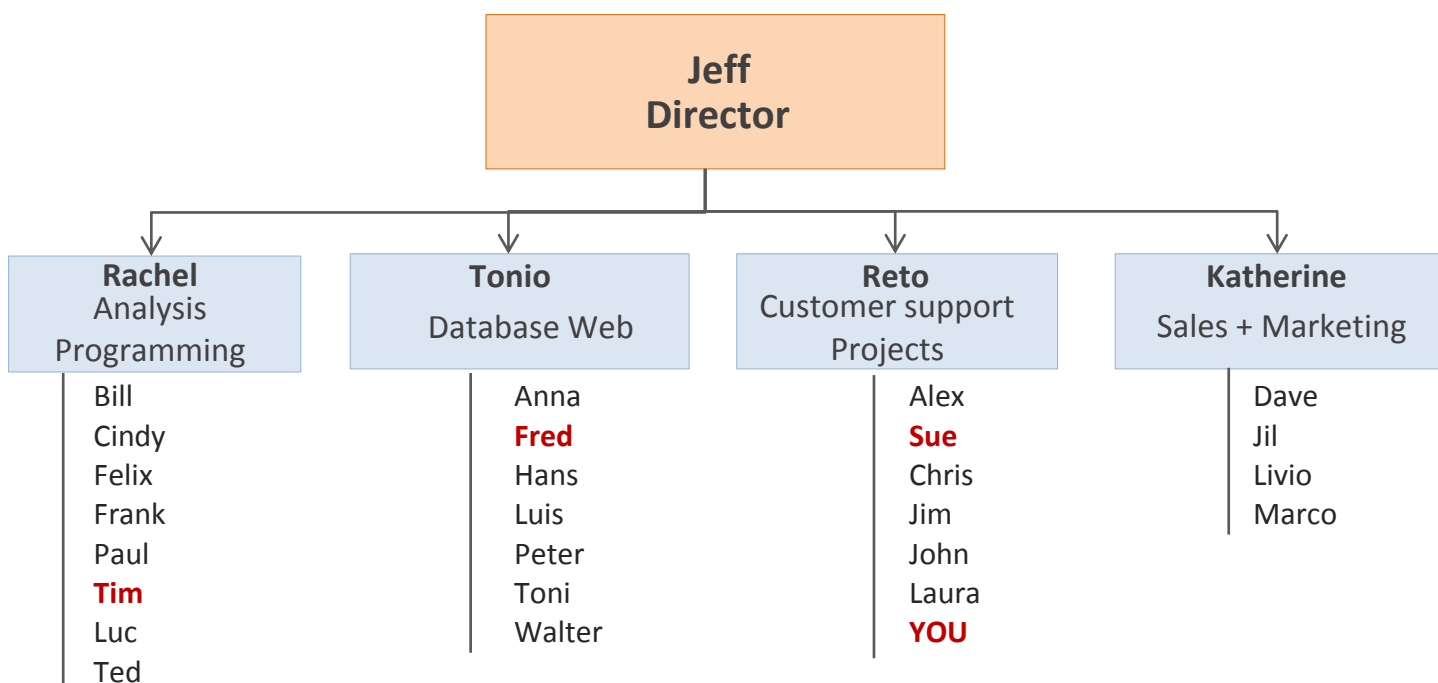

	Backlog Items	Number of people	Estimated duration (days)	Depends on previous activities	Required skills				
					Web Design	Database	Programming	Business	Sales + Mkg
1	Solution Architecture	2	5	—	2			5	3
2	Support Concept	1	7	—	5			2	
3	User Interface	2	10	—	4	2		3	1
4	Database Development	2	12	1	1	6	3		
5	Alpha Release Test	2	8	4	3	1	2	2	2
6	Art Design	2	13	5	5	1	1	3	
7	Search Implementation	4	15	—	3	2	3		
8	Traffic Optimization	3	14	—	1	2	4		
9	Admin tools	3	5	—	5	1	2	1	
10	Release Candidate	1	10	6	3		3	2	
11	Marketing Strategy	2	11	—				4	6
12	eShop Design	3	6	—	3	1	4	2	
13	Marketing Campaign	4	11	11				3	5
14	eShop Deployment	1	5	12	4		1	2	
15	Integration Test	3	3	10	2		1	2	
16	Support Deployment	1	22	2	5			2	
17	General Availability	4	2	15	3		3	2	

	Resources	Hourly rate	Availability for the project	Available from week	Skills				
					Web Design	Database	Programming	Business	Sales + Mkg
	Alex	86	100%	4	3	1	2	2	
	Anna	160	100%	2	6	5	6	3	
	Bill	102	100%	4	3	2	4		2
	Cindy	87	80%	3	2	3	3		
	Felix	89	100%	6	1		4		1
	Fred	89	90%	1	2	4	2		
	Hans	135	80%	2	6	3	5	2	
	John	125	100%	3	4	6	5		
	Livio	97	100%	2	1	1		4	6
	Luc	70	70%	3	2		4		
	Marco	89	100%	3	1			5	5
	Paul	175	100%	4	5	5	6	3	1
	Peter	128	80%	2	6	4	4	1	
	Sue	151	80%	1	5	3	4	5	3
	Ted	58	100%	3	3		3		
	Tim	97	100%	1	2		4	3	

Activity Network

